

Pontyclun Primary School Redevelopment

**MORGAN
SINDALL**
CONSTRUCTION

safe

on time

snag free

delighted client

recommended

Newsletter 4 - March 2023

PROGRESS...

As part of our Phase 1a Works we have carried out the following activities:

- Installed and handed over the First Block of Temporary Classrooms.
- Commenced ground works for the second block of demountable classrooms.

LOOKING FORWARD...


Works that we are planning to undertake in April:

- Installation of second block of temporary classrooms.
- Provide additional temporary hard surfaced play areas

Note: The installation of the new temporary classroom blocks will be carried out during the last 2 days of the Easter Holidays. We will need to transport 18 large units into the school ground, and lift the units into place with mobile cranes. We are unable to undertake this complex work during normal school hours.

We have a temporary traffic order in place for Thursday 13th April & Friday 14th April, to prevent parking in some areas of Palalwyf Avenue. This is necessary to safely deliver the units to site and avoid potential damage to parked cars. Details of the traffic order can be seen, in the drawing to the side.

This will be in operation from 08:00am Thursday 13th April until 1700 Friday 14th April. This means that no parking will be permitted in the areas marked red on the below plan during this period. Normal parking arrangements will resume from 5:00pm Friday 14th April.

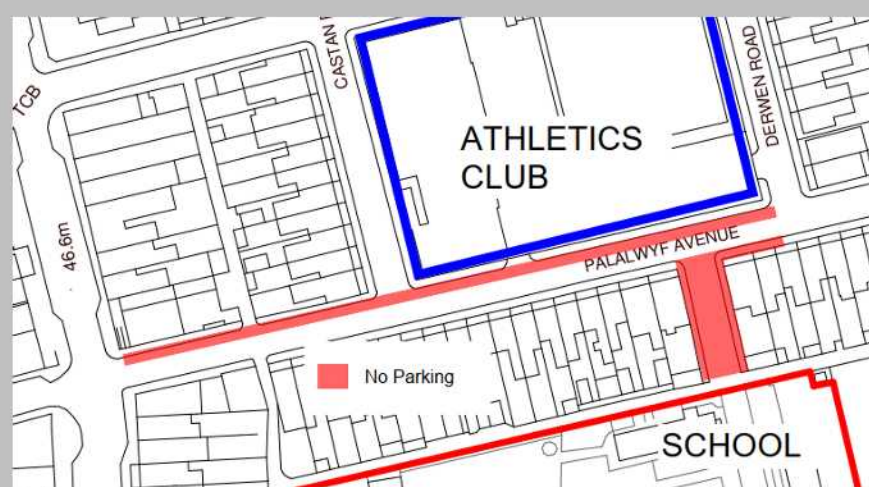

Morgan Sindall Team

If you require further information regarding the project please contact:

- Gareth Morgan, Senior Project Manager:
Email: gareth.morgan@morgansindall.com
Phone: 07989733497
- David Files, Senior Site Manager:
Email: david.files@morgansindall.com
Phone: 07970177896



Cymunedau **Dysgu** Cynaliadwy
Sustainable Communities for Learning



morgansindall.com

in t

@morgansindallci

Boundless possibilities

Aiddatblygu Ysgol Gynradd Pont-y-clun

**MORGAN
SINDALL**
CONSTRUCTION

safe

on time

snag free

delighted client

recommended

Cylchlythyr 4 - Mawrth 2023

CYNNYDD...

Fel rhan o'n Gwaith Cam 1a, rydyn ni wedi gwneud y canlynol:

- Gosod a throsglwyddo Bloc Cyntaf y Dosbarthiadau dros dro.
- Dechrau'r gwaith ar sylfaen Ail Floc y Dosbarthiadau dros dro.

EDRYCH YMLAEN...

Dyma'r gwaith rydyn ni'n bwriadu ei wneud ym mis Ebrill:

- Gosod ail floc y dosbarthiadau dros dro.
- Darparu ardaloedd chwarae wyneb caled ychwanegol dros dro.


Sylwch: Bydd y gwaith o osod y bloc newydd ar gyfer y dosbarthiadau dros dro yn cael ei gynnal yn ystod dau ddiwrnod olaf Gwyliau'r Pasg. Byddwn ni angen cludo 18 o unedau mawr ar safle'r ysgol, a chodi'r unedau hynny i'w lle gyda chraeniau symudol. Nid oes modd i ni allu cwblhau'r gwaith cymhleth hwn yn ystod oriau ysgol gyda chraeniau symudol.

Mae gennym ni orchmynion traffig dros dro ar waith ar gyfer dydd Iau, 13 Ebrill a dydd Gwener, 14 Ebrill er mwyn rhwystro pobl rhag parcio mewn rhai ardaloedd yng Nghoedlan y Palalwyf. Mae'n rhaid gwneud hyn er mwyn danfon yr unedau'n ddiogel ar y safle ac osgoi difrod posib i geir sydd wedi parcio. Mae'r ardaloedd sydd am gael eu heffeithio o ganlyniad i'r cyfyngiadau hyn wedi'u marcio'n goch yn y cynllun Gorchymyn Traffig.

Bydd y cynllun hwn ar waith o 8:00am ddydd Iau, 13 Ebrill hyd at 5:00pm ddydd Gwener, 14 Ebrill. Mae hyn yn golygu na fydd modd parcio yn ystod y cyfnod hwn yn yr ardaloedd sydd wedi'u marcio'n goch yn y cynllun Gorchymyn Traffig. Bydd y trefniadau parcio arferol yn dod yn ôl i rym o 5:00pm ymlaen ddydd Gwener, 14 Ebrill.



Y Cynllun Gorchymyn Traffig...

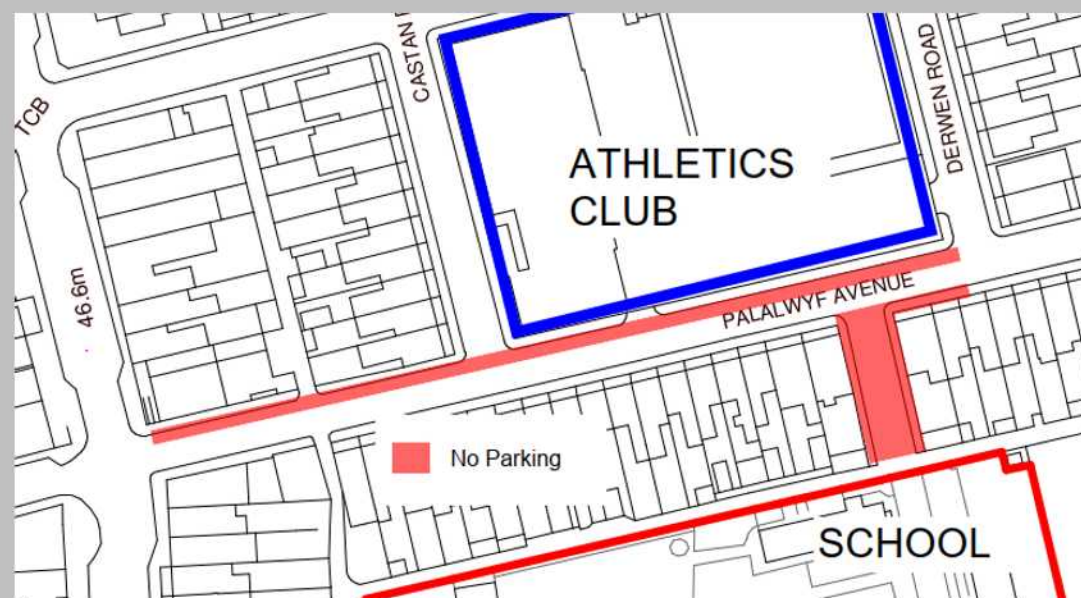

Tîm Morgan Sindall

Os ydych chi eisiau rhagor o wybodaeth am y prosiect, cysylltwch â:

- Gareth Morgan, Uwch Reolwr y Prosiect:
E-bost: gareth.morgan@morgansindall.com
Ffôn: 07989733497
- David Files, Uwch Reolwr y Safle:
E-bost: david.files@morgansindall.com



Cymunedau **Dysgu** Cynaliadwy
Sustainable Communities for Learning



morgansindall.com

in t

@morgansindallci

Boundless possibilities
